WEBSITE PROPOSAL / CLIENT 04

More to Missoula.

LOCAL COMMUNITY LIFE

A friendlier way to discover local activities, people, and places.



Great experiences are easy to miss.

Missoula offers more than sports, but local opportunities can be hard to find in one place.

01

SCATTERED INFORMATION

Activities and events live across different websites, accounts, and flyers.

02

DIFFERENT NEEDS

Not everyone wants the same activities, price points, or schedules.

03

UNCLEAR DETAILS

People need to know where, when, cost, and what to expect before going.

PROJECT GOAL

Help residents find a local activity that fits their interests and circumstances.

One inviting place to explore.

A clear mobile-first website turns scattered possibilities into simple next steps.

01

DISCOVER BY INTEREST

Explore arts, recreation, social activities, and local experiences.

02


DETAILS THAT MATTER

Show timing, price, location, and helpful access information.

03

QUICK WAY FORWARD

Use clear links to organizers and activity details.

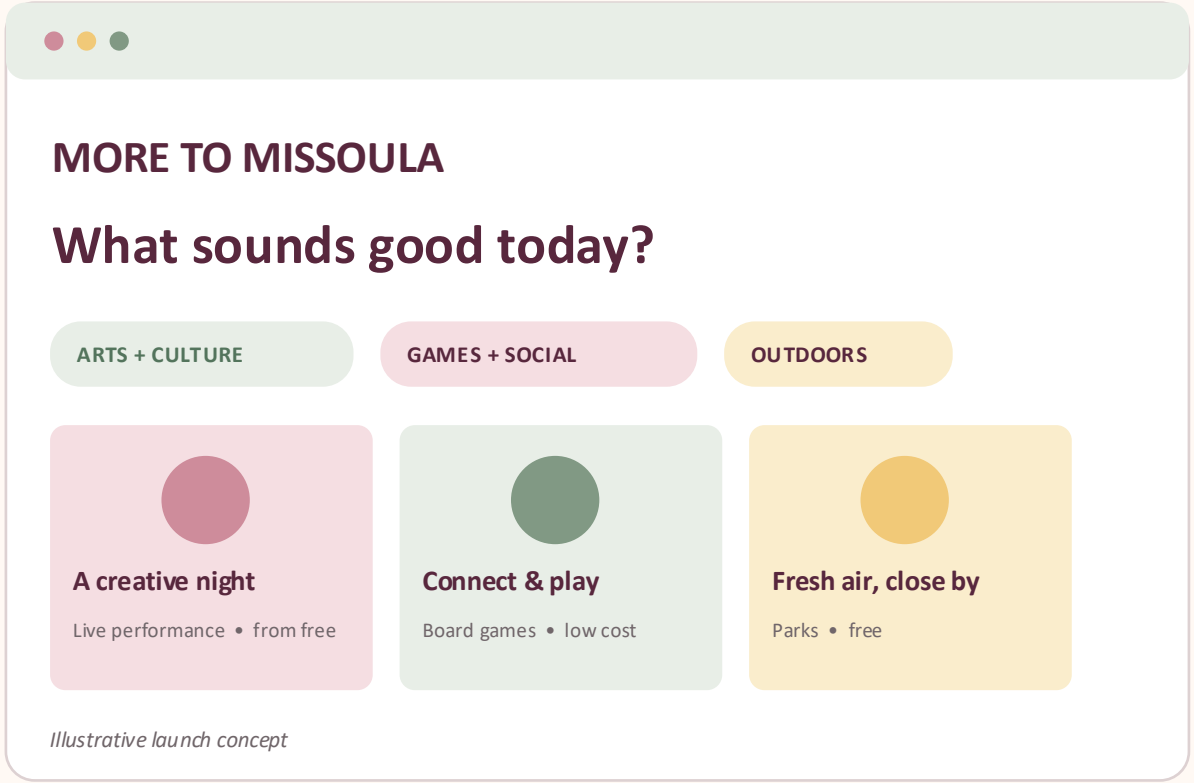

Illustrative launch concept

A focused, four-page launch.

Build the essentials now. Leave complex features for a future phase.

THE FOUR PAGE TYPES

01	**Home**	Inviting introduction and featured options
02	**Discover**	Browsable activity cards and simple filters
03	**Activity Detail**	Reusable template with practical information
04	**About + Get Listed**	Purpose and a contact/submission link

WHAT IS INCLUDED

Responsive design • up to 20 client-supplied listings
Interest and cost filters • basic accessibility checks
2 feedback rounds • up to 3 requested revisions

NOT IN THE 3-WEEK LAUNCH

User accounts, ticketing, live citywide integrations, a full events database, or ongoing content entry.

A clear, fixed-fee estimate.

One designer, a realistic scope, and no surprise features.

PROJECT FEE

$2,700

60 hours × $45/hour

Includes planning, design, site build, testing, and handoff.

ESTIMATED WORK

Discovery + structure	8 hours	**$360**
Visual design	16 hours	**$720**
Website build	27 hours	**$1,215**
Testing + handoff	9 hours	**$405**

Client-paid extras: hosting (~$15–25/mo) and domain (~$15–25/yr), if needed.

Budget illustration for this classroom proposal; platform costs vary.

Three weeks. Clear checkpoints.

The short turnaround depends on timely client materials and feedback.

WEEK 01

Align & sketch

Kickoff and content inventory
Site structure and early layouts
Confirm design direction

CLIENT FEEDBACK 01

WEEK 02

Design & build

Approve visual screens
Build four responsive page types
Add discovery filters

CLIENT FEEDBACK 02

WEEK 03

Polish & launch

Complete scoped revisions
Test key pages and interactions
Handoff and publish


FINAL APPROVAL

Scope control: 2 client feedback rounds + up to 3 client-requested revisions in total after direction is agreed upon.

Client provides approved content/assets early and responds to each review within two business days.

Four page types. One clear path.

The sitemap keeps the original launch focused, while linking interest browsing to one shared activity template.

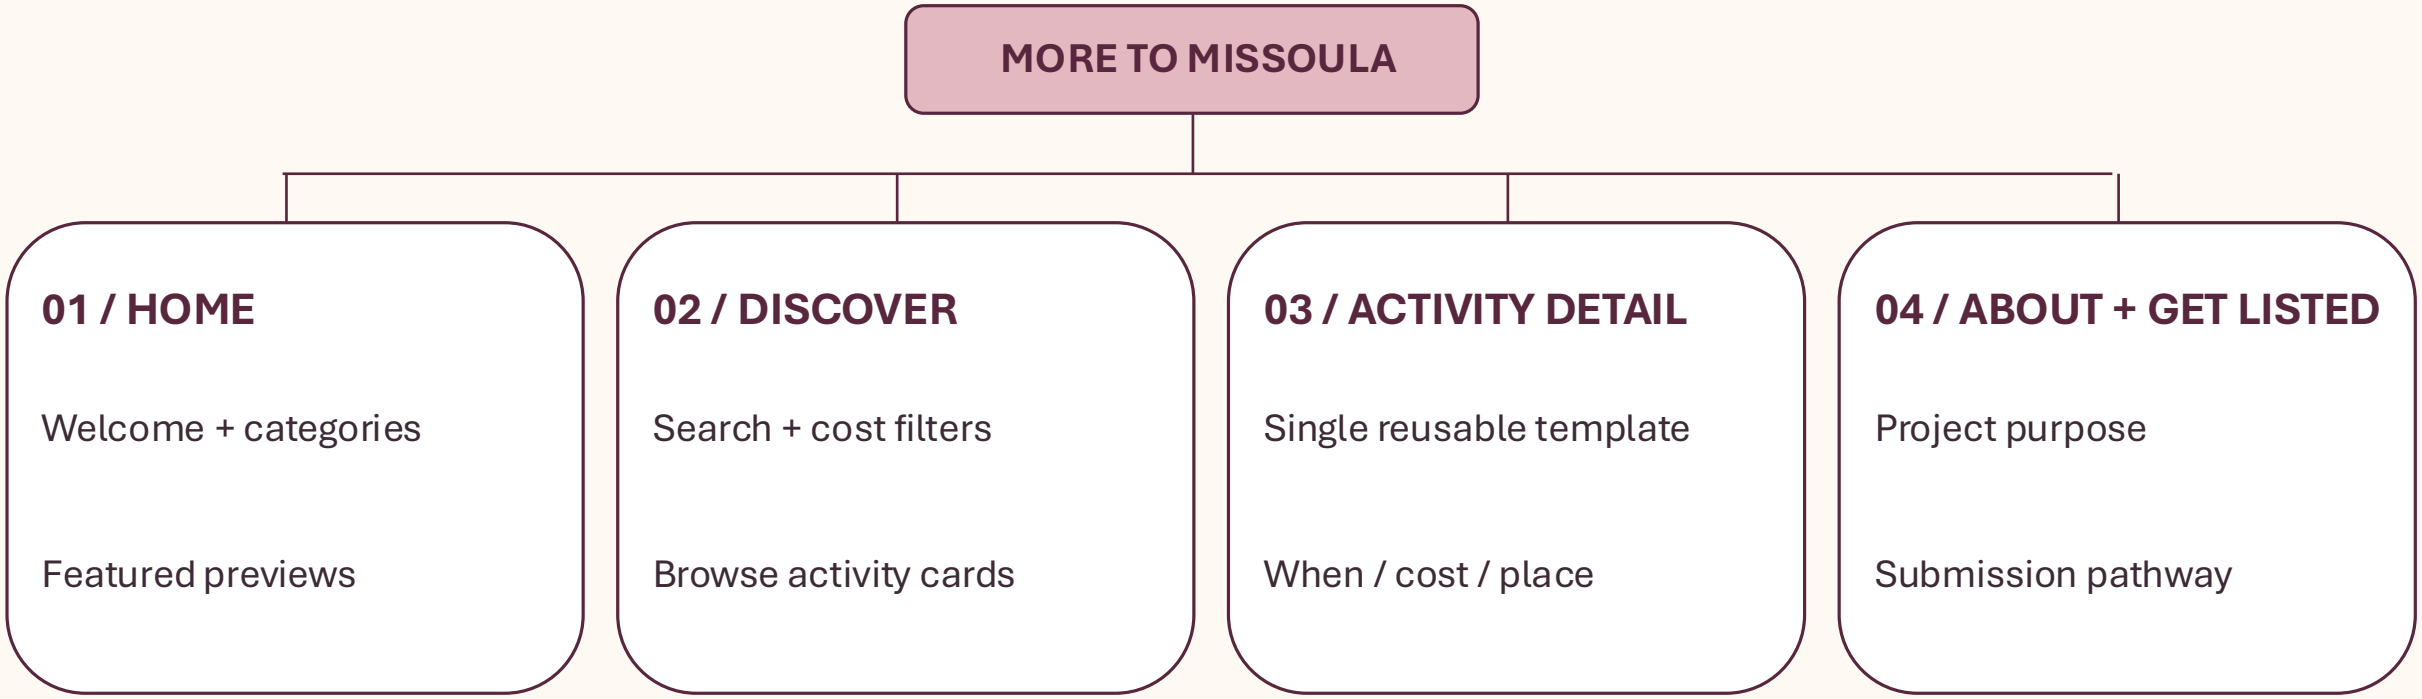

Discover cards link to Activity Detail using a unique listing ID.

Same scope. Clearer interactions.

Wireframing clarified page responsibilities without adding high-risk features or new deliverables.

HOME	Lead with “What sounds good today?” and three interest pathways.
DISCOVER	Place search and interest/cost filters next to reusable activity cards.
DETAIL	Use one template for all approved listings instead of unique page builds.
ABOUT	Explain the Get Listed process; add a contact link after approval.

Prototype listings are illustrative—not verified public events.

UNCHANGED COMMITMENTS

$2,700

Three-week classroom estimate

- Four page types
- Up to 20 approved listings
- Two feedback rounds
- Up to three requested revisions

Build once. Reuse thoughtfully.

A component-based estimate makes the three-week scope easier to manage.

ESTIMATED WORK	HOURS	COST
Discovery + sitemap + four wireframes	8	$360
Shared visual system + four page designs	16	$720
Reusable HTML/CSS components + filters + detail	27	$1,215
Responsive checks + testing + handoff	9	$405

Reuse: nav, footer, buttons, category/activity cards • New: filters + dynamic detail

Planning estimate only; confirm assumptions against the Project 1 postmortem.

60 HOURS / $2,700

Let’s make more of Missoula discoverable.

A thoughtful first version can open the door to more community participation.

01 Approve the plan

Confirm the four-page scope and $2,700 fixed fee.

02 Share starter content

Provide branding, photos, and up to 20 approved listings.

03 Schedule kickoff

Meet for 30 minutes to align goals and responsibilities.

THE THREE-WEEK CLOCK STARTS AFTER APPROVAL AND CONTENT HANDOFF.
